

Construction Update #7

September 5th, 2017

Watermain Replacement on Heath Street West from Lower Village Gate to Spadina Road


Contract #: 16ECS-LU-18SU
Revised Start Date: March 20, 2017
Original End Date: August, 2017
New End Date: October 13, 2017
*Timeline is subject to change.

Due to unexpected conditions with the existing watermain, the project will now be finished by **October 13, 2017**.

Remaining water service connections and branch connections will be completed and road restoration will begin shortly. In order to facilitate the remaining work, there will be ongoing local lane closures along Heath Street West from Tweedsmuir Avenue to Spadina Road.

We appreciate your patience and understanding during this project and as we finish the restoration.

MAP OF WORK AREA

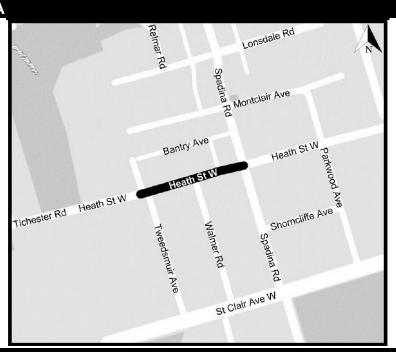

WORK UPDATE

To date the contractor has:

- · Completed the installation of the watermain mainline
- Begun the transfer of water service connections onto the new watermain
- Begun connections on the new watermain to the existing watermain system

The contractor will:

- Complete the transfer of the remaining service connections onto the new watermain
- Complete the remaining connections of the new watermain to the existing watermain system
- Complete restoration within the road and sidewalk above the watermain and services
- Complete restoration of the concrete intersection at Lower Village Gate and Heath Street West

WHAT TO EXPECT DURING CONSTRUCTION

- You may experience dust, noise, water shut-offs and other inconveniences. The City will make
 efforts to reduce the impacts. Your patience is appreciated.
- Property owners should remove items located within the City property limits (boulevard), such as landscaping and / or decorative objects. If you have a sprinkler system within the boulevard, please contact the Field Ambassador.
- The City will not be responsible for damage to any privately owned items on City property.



Construction Update #7



Work Hours: Work will take place from 7:00 am to 7:00 pm, Monday to Friday, with work after hours and on weekends as required.



Water Service Disruptions: From time-to-time, the water supply to your property will be shut-off to complete construction; the contractor will provide at least 24-hour advance notice. Throughout the work, it is recommended that you temporarily disconnect any water treatment systems (i.e. softeners or filters), water-cooled air conditioners or similar plumbing fixtures. Automatic lawn sprinkler systems may also be affected, therefore, you may need to water manually. In the event you did not received advanced notice, an *emergency water shut off* could have been necessary.



Road and Sidewalk Access: In order to complete the work in a safe manner, there will be road and sidewalk restrictions within the construction work area.



Driveway Access: The contractor will notify you of any temporary restrictions to your driveway access. If your property has two entrances, one entrance will be kept open at all times. Access for emergency vehicles will be maintained at all times.

Accommodation: Residents that require accommodation must contact the Field Ambassador to arrange for access during the construction period.



Traffic Management: Efforts have been made to manage traffic in the area for the safety of workers, road users and residents. Road users should expect delays and increased traffic on nearby main and side streets.

Traffic on Heath Street will be reduced to one lane for the duration of construction activities.



Parking: Parking in the active work zone is not permitted due to space requirements for construction equipment and materials. If your parked vehicle affects the construction work, it will be re-located with no charge to the owner. Please contact parking control for the location of your vehicle at **416-808-2222**.

13K On-Street Parking Permit holders are asked to park elsewhere within the 13K parking zone (Heath Street West and Tichester Road from Bathurst Street to Spadina Road) to accommodate construction activity.



Garbage & Recycling: Please follow your normal routine. If required, the contractor will move bins to an appropriate location and return them. *Please ensure that you label your bins with your address.*



Restoration: Areas affected by construction will be restored. Only the portions of road dug for the watermain trench will be restored; road resurfacing (from curb to curb) is not part of this project.

NEED MORE INFORMATION:

If you have questions about the upcoming work, please contact us and quote Contract # 16ECS-LU-18SU

Field Ambassador	Ilham Musafere: 416-473-5799, Field.Ambassador.PM3B@ghd.com
TTY Hearing Impaired Service	416-338-0889
	(7 Days a week, 8:00 am - 5:00 pm, closed holidays)
General inquiries	311
Website	www.toronto.ca/improvements/ward21.htm

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
