December 14, 2022

Jane Street Culvert Replacement over Black Creek

Contract: 22ECS-BE-02BSE


Construction began on October 25, 2022 and will be completed by June, 2023* *Timeline is subject to change.

This notice provides an update on the contractor's working hours.

The City's contractor will begin working extended hours from 7 p.m. to 11 p.m. for specific construction tasks in order to expedite the work and minimize the inconvenience to the public. The first tasks involve the installation of roadway protection (sheet piling) and excavation, which involves some noise and vibration.

We realize that this project has an impact to businesses and residents along Jane Street. We appreciate your patience and apologize for inconvenience.

MAP OF WORK AREA

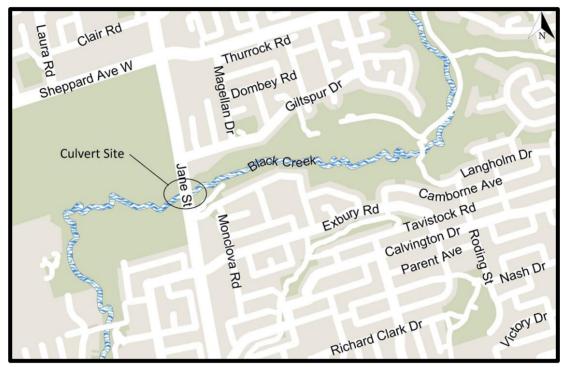

WORK STATUS TO DATE

The City's contractor has:

- Completed a temporary widening on the east side of Jane Street for the traffic staging.
- Removed all trees needed to facilitate construction of the new culvert and the creek restoration/erosion protection measure.
- Implemented the first stage of the traffic control in order to work on the west half of Jane St.
- Removed asphalt on the west half of Jane St.

REMAINING WORK

- Installation of a protection system for the active portion of the roadway.
- Excavation on west side of Jane Street.
- The contractor will proceed with excavation to the foundation level of the culvert.
- Install temporary flow passage system for the creek.
- Remove and bypass existing sanitary sewer.
- Install all culvert components
- Install new sewers connected to the culvert.
- Backfill and pave.
- Switch traffic to the west half of Jane St to repeat the construction on the east half.

WHAT TO EXPECT DURING CONSTRUCTION

• You may experience dust, noise and other inconveniences. The City will make efforts to reduce the impacts and apologize for any inconveniences. We appreciate your patience.

Interview Construction Update No.1

Ŀ	Accessible Accommodation: The City's contractor must ensure safe and accessible walkways and entryways are maintained for everyone during construction. Any temporary access disruptions will be communicated as soon as possible. If you experience a disruption, have a specific access need or related accommodation request, contact the Project Manager listed below.
	Restoration: The construction work area will be restored with sod, concrete and/or asphalt - where required. Interlocking bricks, flagstone on a granular base, or other similar features that are removed from public and private property during construction will be replaced. Lawn seeding and/or laying of sod will be done as needed during the spring (April to June) and fall (September to October).

LOOKING FOR MORE INFORMATION?

If you have questions about this construction project, please contact staff listed below.

Contract	22ECS-BE-02BSE
Project Manager	Jeffrey Atsalinos, 416-392-4587, Jeffrey.Atsalinos@toronto.ca
TTY Hearing Impaired Service	416-338-0889 (Daily - 8 a.m. to 5 p.m., closed holidays)
General inquiries	311
Website	toronto.ca/yorkcentre toronto.ca/humberriverblackcreek

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
