

April 12, 2023


Watermain Replacement and Road Resurfacing on Canfield Place

Contract: 22ECS-LU-07SU
Start Date: August 10, 2022
Restart Date: April 24, 2023
End Date: June 5, 2023
**Timeline is subject to change.*

This notice provides an update on the replacement of the watermain and the City-owned portion of substandard water services on Canfield Place. Work on this project is currently behind schedule. Since the remaining work can only be completed during favourable weather conditions, the restoration activities are expected to resume on April 24, 2023, and has an end date of June 5, 2023.

We know this project has an impact to all businesses and residents along Canfield Place. We sympathize and appreciate your patience with the dust, noise, fencing and other inconveniences.

MAP OF WORK AREA

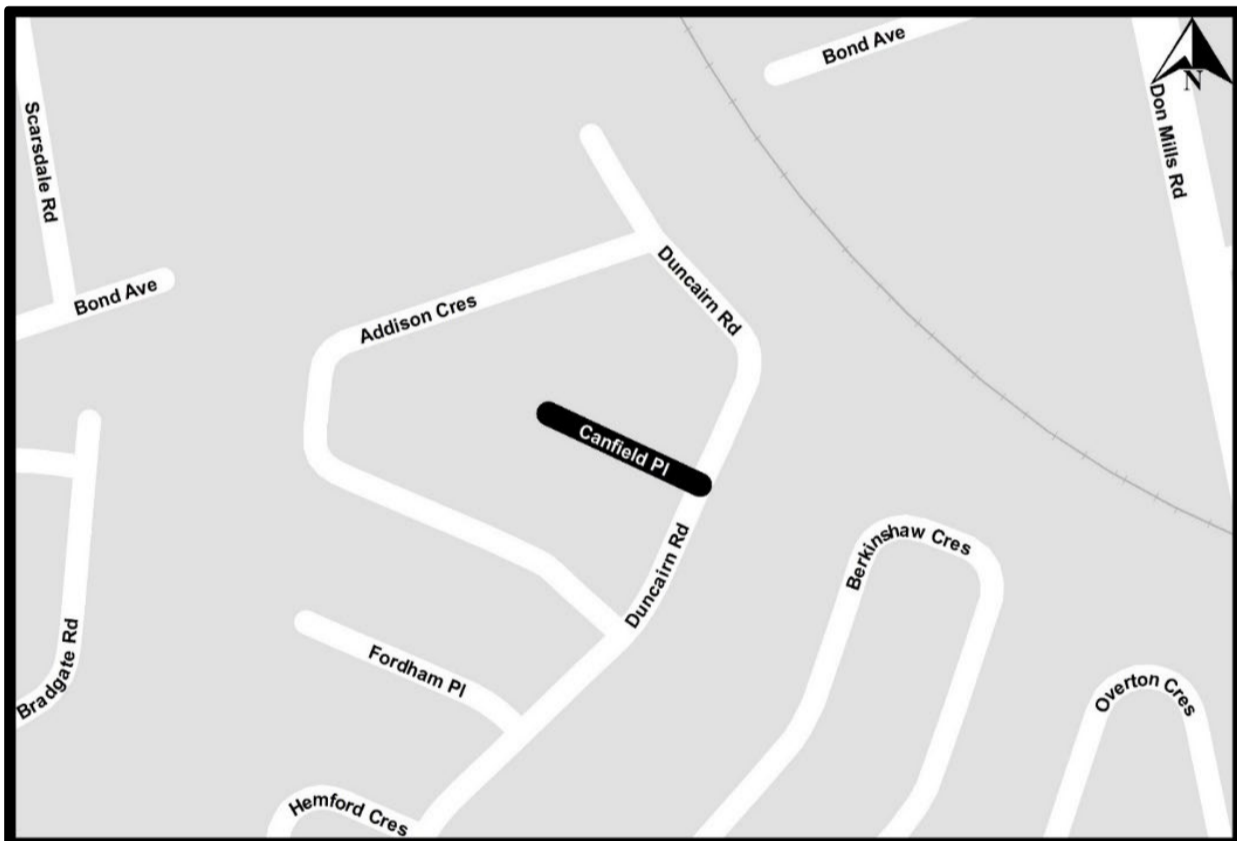

WORK STATUS TO DATE

The City's contractor has:

- Completed the watermain installation.
- Completed the water service connections.
- Completed temporary restoration.
- Completed permanent restoration of concrete sidewalks, curbs, and driveways.

REMAINING WORK

The City's contractor will complete:

- Milling of asphalt, utility adjustments and base repairs.
- Paving of asphalt.
- Routing and sealing, and pavement marking.
- Sod repairs.

NEED MORE INFORMATION?

If you have questions about this construction project, please contact staff listed below. If you need to speak with staff on the construction site – please ask for the site inspector, respect physical distancing and wear a mask.

Contract	22ECS-LU-07SU
Field Ambassador	Sunil Issac, 289-314-3127, field.ambassador2@GHD.com
TTY Hearing Impaired Service	416-338-0889 (Daily 8 a.m. to 5 p.m., closed holidays)
General inquiries	311
Website	toronto.ca/DonValleyEast

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
