

September 11, 2023


West Humber Sanitary Trunk Sewer Rehabilitation

Contract: 21ECS-LU-07TT
 Expected Start Date: September 2022 Expected End Date: June 2023
 NEW End Date: October 20, 2023
**Timeline is subject to change.*

This notice provides an update on the rehabilitation of a section of the West Humber Sanitary Trunk Sewer (STS) from Humber Gate Park to Esther Lorrie Park. The sewer is located mainly along the West Humber Trail. The sanitary trunk sewer is an underground pipe that collects wastewater from sewers and delivers it to wastewater facilities for treatment. Work on this project is currently behind schedule. This delay was caused by additional emergency work due an unforeseen condition of the incoming sideline sewers that needed immediate attention.

We know this project has an impact to all businesses and residents along the West Humber Trail, from Humber Gate Park to Esther Lorrie Park. We appreciate your patience with the dust, noise, fencing and other inconveniences.

MAP OF WORK AREA

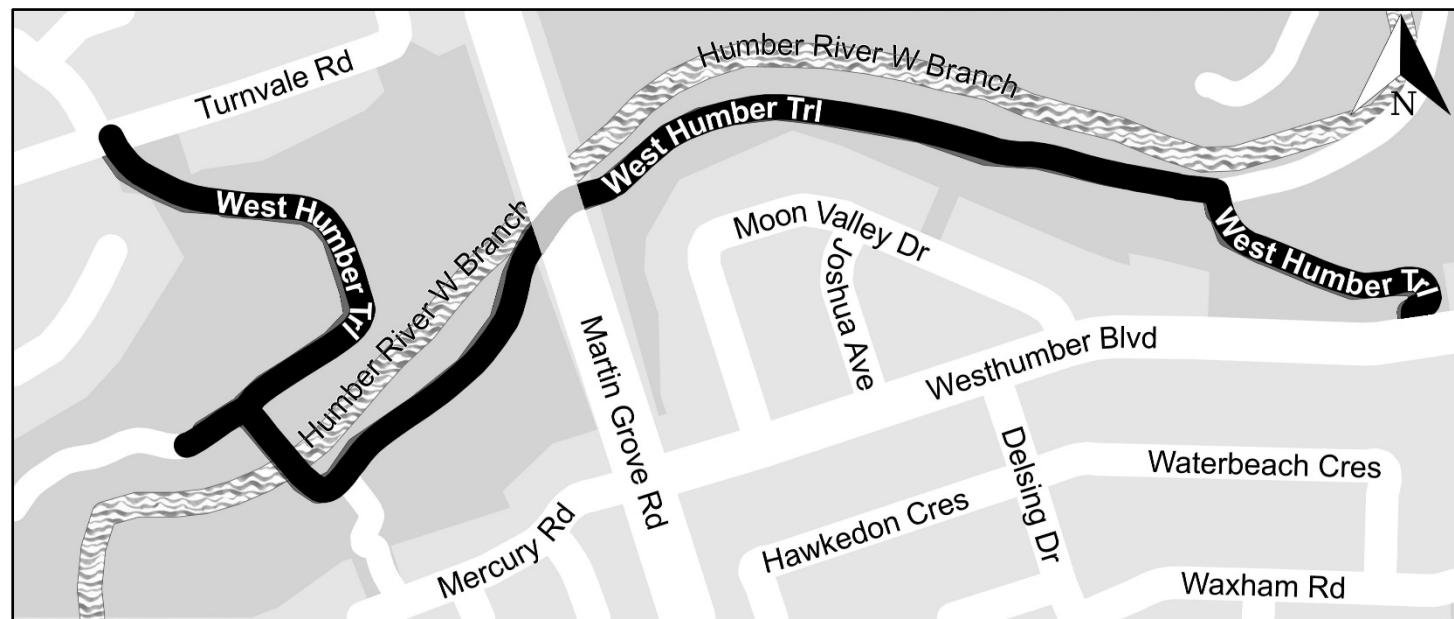

WORK STATUS TO DATE


- The emergency work is completed
- The trunk sewers’ rehab work is currently being performed and has been mostly completed.







REMAINING WORK

- The contractor will restore work zone and resurface the affected locations on the trail by October 20, 2023 (weather permitting for new asphalt)

WHAT TO EXPECT DURING CONSTRUCTION

- You may experience dust, noise and other inconveniences. The City will make efforts to reduce the impacts. We appreciate your patience.
- The City will not be responsible for damage to any privately owned items on City property.

	Work Hours: Work will take place from 7 a.m.to 7 p.m., Monday to Friday, with work after hours and on weekends as required.
---	--

	Sewer Service Disruptions: If the sanitary sewer service from your property requires a disruption to complete repairs the contractor will provide at least 24-hour advance notice. During sanitary sewer service disruptions, you will be advised to limit your water use.
	Road and Sidewalk Access: In order to complete the work in a safe manner, there will be road and sidewalk restrictions within the work zone. Access for emergency vehicles will be maintained at all times.
	Accessible Accommodation: The City's contractor must ensure safe and accessible walkways and entryways are maintained for everyone during construction. Any temporary access disruptions will be communicated as soon as possible. If you experience a disruption, have a specific access need or related accommodation request, contact the Project Manager listed below.
	Parks and Trails: Due to the nature of this work a section of the West Humber trail and Esther Lorie Park will be affected. Sections of the park, fields and trail will be fenced off and closed for public safety. Signs will be posted. All areas of the park and trail affected by construction will be restored.
	Cyclists: If travelling along the trails, please follow the detour signs in the active work zones.
	Restoration: The construction work area will be restored with sod, concrete and/or asphalt where required. Lawn seeding and/or laying of sod will be done as needed during ideal growing seasons only - in the spring (April to June) and fall (September to October).

NEED MORE INFORMATION?

If you have questions about this construction project, please contact staff listed below. If you need to speak with staff on the construction site – please ask for the site inspector, respect physical distancing and wear a mask.

Contract	21ECS-LU-07TT
Project Manager	Mustafa Mufty, 416-392-8424, Mustafa.Mufty@toronto.ca
TTY Hearing Impaired Service	416-338-0889 (Daily 8 a.m. to 5 p.m., closed holidays)
General inquiries	311
Website	toronto.ca/ward-1

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait
