

Construction Update #1

June 14, 2021

Watermain Replacement on Broadview Avenue from Danforth Avenue to Gerrard Street East

Contract: 21ECS-TI-13SP Expected Start Date: May 10, 2021 Expected End Date: Spring, 2022

*Timelines are subject to change and future notice will be provided.

Unfortunately, due to an ongoing industry wide watermain pipe shortage, construction on the Broadview watermain project will be delayed until such time as the material is available which is anticipated to arrive at the end of July. This material delay will impact the project completion date, which is now estimated to be completed in spring 2022. Current work taking place on Montcrest Avenue has not been impacted by this material shortage and is expected to be completed during the week of June 28.

Broadview Watermain work may not commence until approximately late July or early August 2021. Once all pipes and materials can be secured by our contractor a revised project schedule and a Construction Update will be issued. Our construction team will re-engage with the local community regarding preparing for local construction impacts. During the delay time our contractor will be demobilizing in certain areas along Broadview Avenue to allow for restaurant patios, on street parking, and short term parking for deliveries.

Restaurants participating in the CAFÉ TO program will be allowed to install temporary patios during the construction delay. All other projects scheduled for this area are still on schedule, please see Other Work in Area chart for all project status updates.

IMPORTANT INFORMATION ABOUT COVID-19 AND CONSTRUCTION WORK IN TORONTO


During construction, the contractor is responsible for the Health & Safety on site under the Ontario Occupational Health and Safety Act and is expected to implement COVID-19 mitigation practices. For more information on the City's response to COVID-19 please visit toronto.ca/covid-19.

OTHER WORK IN THE AREA

Project	Status Update
Toronto Hydro Duct Bank Replacement Start: April 5, 2021 End: June 30, 2021	 Toronto Hydro Duct work is progressing on schedule, the eastbound curb lane on Gerrard Street is expected to be reopened by the beginning of July.
Danforth/Royal (DVP Ramp) Bike Lane and Traffic Signal Upgrade Start: April 21, 2021 End: June 30, 2021	The Danforth/Royal Bike Lane and Signal Installation project is on track to begin in June. June start date TBD by Transportation Services.
Prince Edward Viaduct Suicide Prevention Barrier Repairs July- August 2021	 The suicide barrier repair work is on track to start in early July and is expected to be completed by September 2021.
TTC Castle Frank Station Easier Access Program Start: Summer 2021 End: 2024	A TTC Pre Construction Notice will be issued within the coming weeks with a project timeline and exact start dates. The project is on track to start on time.

Construction Update #1

MAP OF WORK AREA

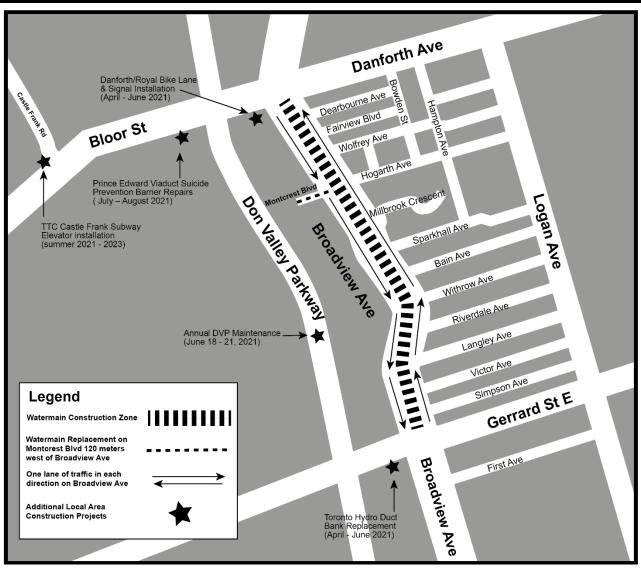

NEED MORE INFORMATION?

If you have questions about the upcoming work, please contact us and quote Contract 20ECS-LU-19SU

Public Consultation Unit	Paul Martin, 416 392-3074, bloorstreetconstruction@toronto.ca
TTY Hearing Impaired Service	416-338-0889 (7 Days a week, 8 a.m. – 5 p.m., closed holidays)
General & after hour inquiries	311
Website	toronto.ca/broadviewconstruction

如果需要普通话协助,请拨 311 如果需要廣東話協助,請致電 311 Sign up to receive construction updates:

toronto.ca/broadviewconstruction

Thank you for your patience. Better infrastructure for all of us is worth the wait.
