

October 5, 2018

## Transmission Watermain Relining on Macpherson Avenue, Boulton Drive and Russell Hill Road


**Contract: 16ECS-LU-01TT**  
**Start Date: March 8, 2017**  
**New End Date: October 31, 2018**  
*\*Timeline is subject to change.*

The City of Toronto is relining the transmission watermains on Macpherson Avenue, Russell Hill Road and Boulton Drive and a local watermain on Boulton Drive (see map).

Majority of the construction work is complete. The Transmission Main on Macpherson Avenue and local watermain on Boulton Drive are back in service. The contractor is working at the two valve chambers shown on the map. The completion of these two chambers and subsequent testing and disinfection are slightly delayed and is expected to be completed by October 31, 2018. This delay was caused by issues crews faced isolating the watermain earlier during construction.

All roads are open for vehicular traffic and cyclists.

### MAP OF WORK AREA

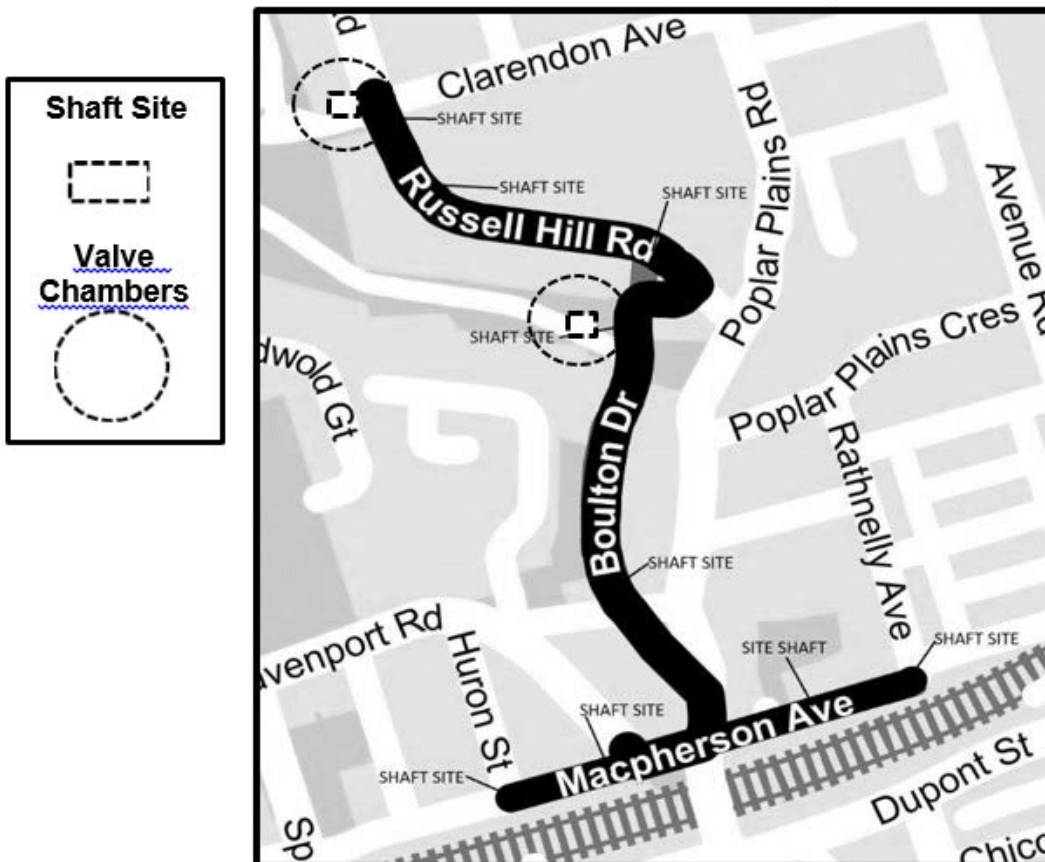

## WORK DETAILS AND STATUS

- The contractor is working at the two chambers circled in the map.
- Once the chambers are constructed, the contractor will be pressure testing and disinfecting the main followed by putting it back to service.
- The contractor will also restore the road and sod areas affected by construction.

## WHAT TO EXPECT DURING CONSTRUCTION

- There will be no impact to water service and vehicular traffic due to this work.
- Construction activity will be primarily limited at the two shaft locations.
- We appreciate your patience while the remaining work is completed.

## NEED MORE INFORMATION?

If you have questions about the upcoming work, please contact us and quote

### Contract 16ECS-LU-01TT

<b>Field Inspector</b>	Mike Hosseini, 647-280-7187, email: <a href="mailto:mike.hosseini@wsp.com">mike.hosseini@wsp.com</a>
<b>Project Manager</b>	Niko Kalo, 416-338-5558, email: <a href="mailto:niko.kalo@toronto.ca">niko.kalo@toronto.ca</a>
<b>TTY Hearing Impaired Service</b>	416-338-0889 (7 Days a week, 8 a.m. to 5 p.m., closed holidays)
<b>General inquiries</b>	311
<b>Website</b>	<a href="http://toronto.ca/improvements/ward22.htm">toronto.ca/improvements/ward22.htm</a>

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
