

August 13, 2021

Watermain Replacement on Broadview Avenue from Danforth Avenue to Gerrard Street East

Contract: 21ECS-TI-13SP
Expected Start Date: May 10, 2021
Expected End Date: Spring, 2022

**Timelines are subject to change and future notice will be provided.*

As watermain installation work continues on Broadview Avenue, please note that heavy construction activity will be continuing in the Broadview Avenue and Danforth Avenue area. Our contractor has recently received another shipment of pipe and will begin installing 180 metres of watermain pipe starting near Loblaw's, moving north to Danforth Avenue. We expect this work to be completed by August 20th. While working in the Broadview Avenue and Danforth Avenue area our contractor will create and maintain delivery and drop off zones for business along this stretch through the remainder of the work.

From August 20th to 27th the contractor will be flushing and pressure testing the new watermain. During this time there will be minimal activity on the construction site. Test results are expected the week of September 3rd. Once all regulatory testing is passed our contractor will begin to transfer the water services to the new watermain. This work is scheduled to start during the week of September 6th to September 11th

Once all service connections are complete in the Broadview Avenue and Danforth Avenue area, watermain installation will continue from Montcrest Avenue working south towards Gerrard Street. Prior to any water service disruption, residents will be notified two days (48hrs) prior to disruption by our contractor. All other projects scheduled for this area are still on schedule, please see Other Work in Area chart for all project status updates.


IMPORTANT INFORMATION ABOUT COVID-19 AND CONSTRUCTION WORK IN TORONTO

During construction, the contractor is responsible for the Health & Safety on site under the Ontario Occupational Health and Safety Act and is expected to implement COVID-19 mitigation practices. For more information on the City's response to COVID-19 please visit toronto.ca/covid-19.

OTHER WORK IN THE AREA

Project	Status Update
Toronto Hydro Duct Bank Replacement Start: April 5, 2021 End: mid-September, 2021	<ul style="list-style-type: none"> Toronto Hydro Duct worked has slowed due to an unforeseen issue with installation, this work is expected to take an additional four weeks to complete.
Prince Edward Viaduct Suicide Prevention Barrier Repairs Start Date: July 5 th End date mid-October	<ul style="list-style-type: none"> The City of Toronto is currently rehabilitating the pedestrian safety and suicide prevention barrier on the Bloor Street Bridge
TTC Castle Frank Station Easier Access Program Start: Summer 2021 End: 2024	<ul style="list-style-type: none"> The project is currently on track to begin by late September 2021. An updated construction notice will be provided by TTC prior to construction start. See TTC.ca for more details.

MAP OF WORK AREA

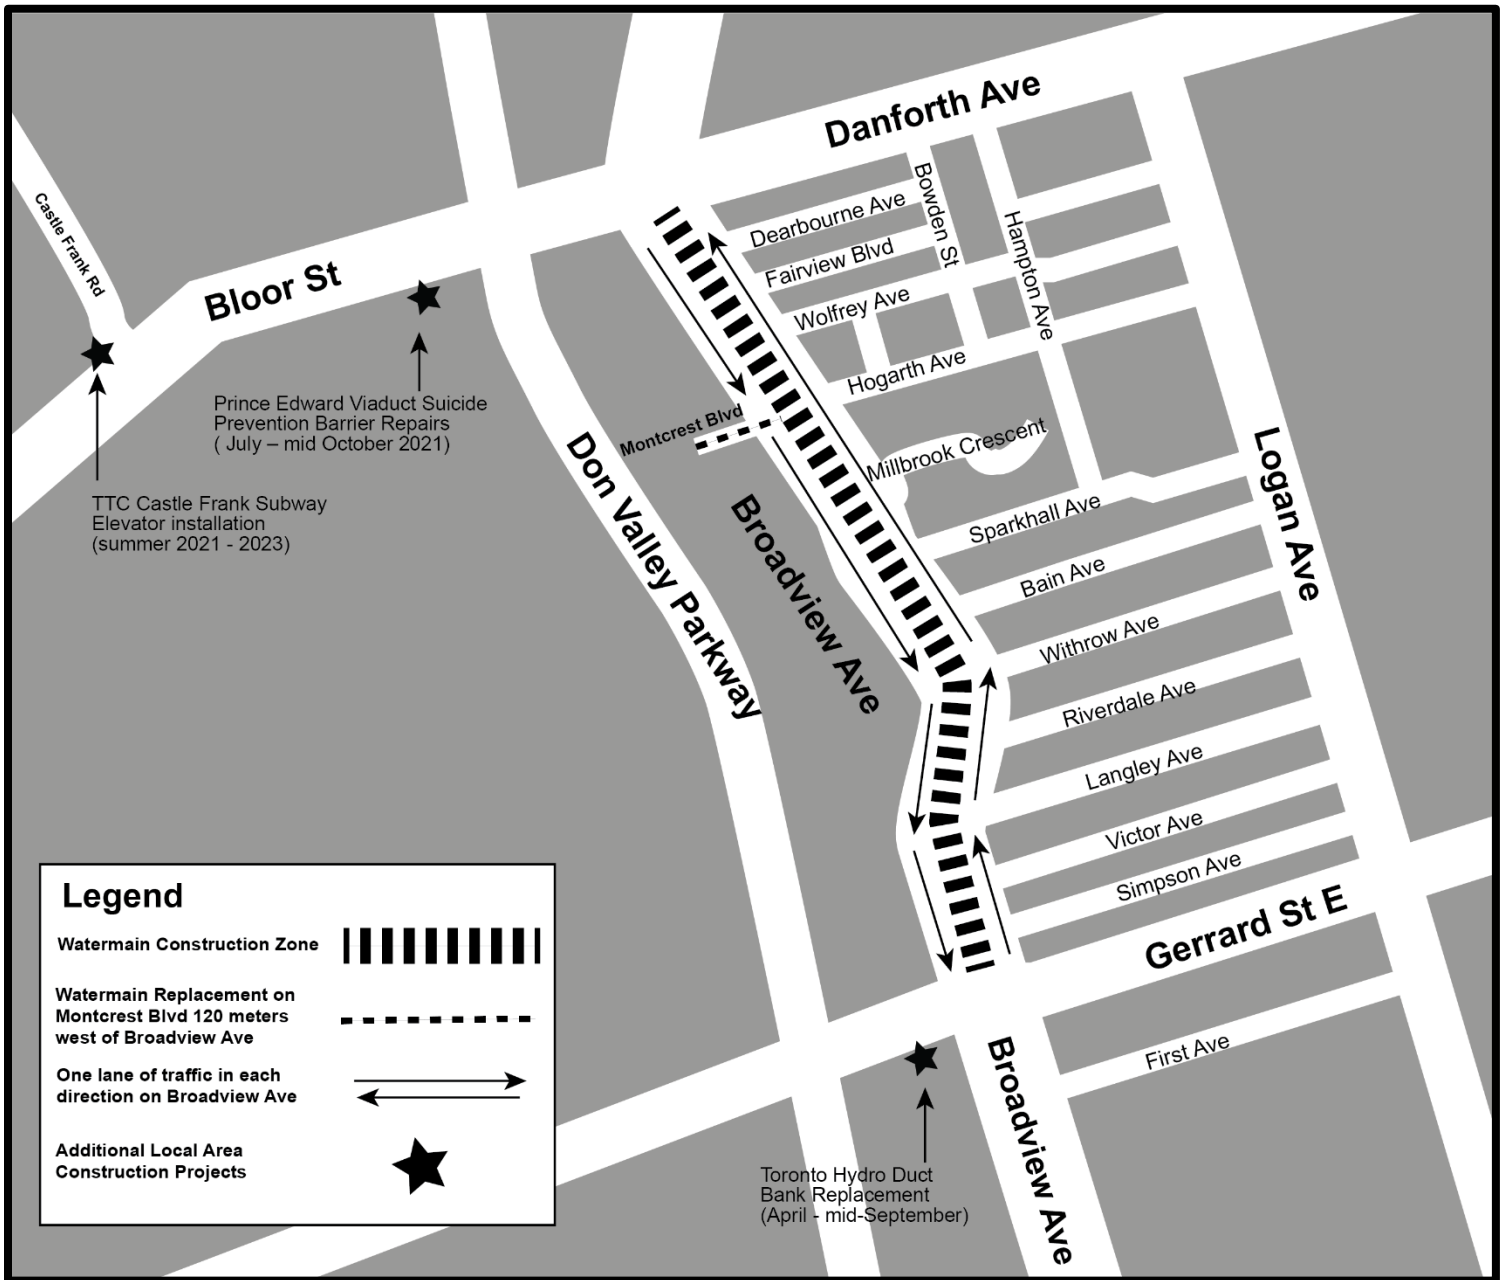

NEED MORE INFORMATION?

If you have questions about the upcoming work, please contact us and quote Contract **20ECS-LU-19SU**

Public Consultation Unit	Paul Martin, 416 392-3074, broadviewconstruction@toronto.ca
TTY Hearing Impaired Service	416-338-0889 (7 Days a week, 8 a.m. – 5 p.m., closed holidays)
General & after hour inquiries	311
Website	toronto.ca/broadviewconstruction

如果需要普通话协助, 请拨 311
 如果需要廣東話協助, 請致電 311

Sign up to receive construction updates:
toronto.ca/broadviewconstruction

Thank you for your patience. Better infrastructure for all of us is worth the wait.
