

October 13, 2021

Road Reconstruction & Green Infrastructure Installation on Winnett Avenue from Durham Avenue to Arlington Avenue

Contract: 20ECS-TI-02LR

Start Date: July 12, 2021; Expected End Date: August 30, 2021

NEW End Date: Summer 2022

Winter Break: December 2021 to April 2022

**Timeline is subject to change.*

This notice provides an update on the progress of City construction on Winnett Avenue from Durham Avenue to Arlington Avenue. Due to issues relating to the material supply of PVC pipe required for the Green Infrastructure component, a portion of the project will be deferred to the spring of 2022.

Temporary restorations within the roadway will be completed by the end of November so as to maintain safe access throughout the winter period. When work restarts in the spring of 2022, the contractor will complete the reconstruction of the road and installation of Green Infrastructure.

An additional Construction Update notice will be provided prior to the start of construction in the spring of 2022.

IMPORTANT INFORMATION ABOUT COVID-19 AND CONSTRUCTION WORK IN TORONTO

During construction, the contractor is responsible for the Health & Safety on site under the Ontario Occupational Health and Safety Act and is expected to implement COVID-19 mitigation practices. For more information on the City's response to COVID-19 please visit toronto.ca/covid-19.

WORK STATUS TO DATE

The City's contractor has:


- Replaced substandard water services
- Replaced curb and sidewalk

REMAINING WORK

In spring of 2022, the contractor will:

- Complete reconstruction of the road base and new asphalt
- Install green infrastructure (permeable pavers)

MAP OF WORK AREA

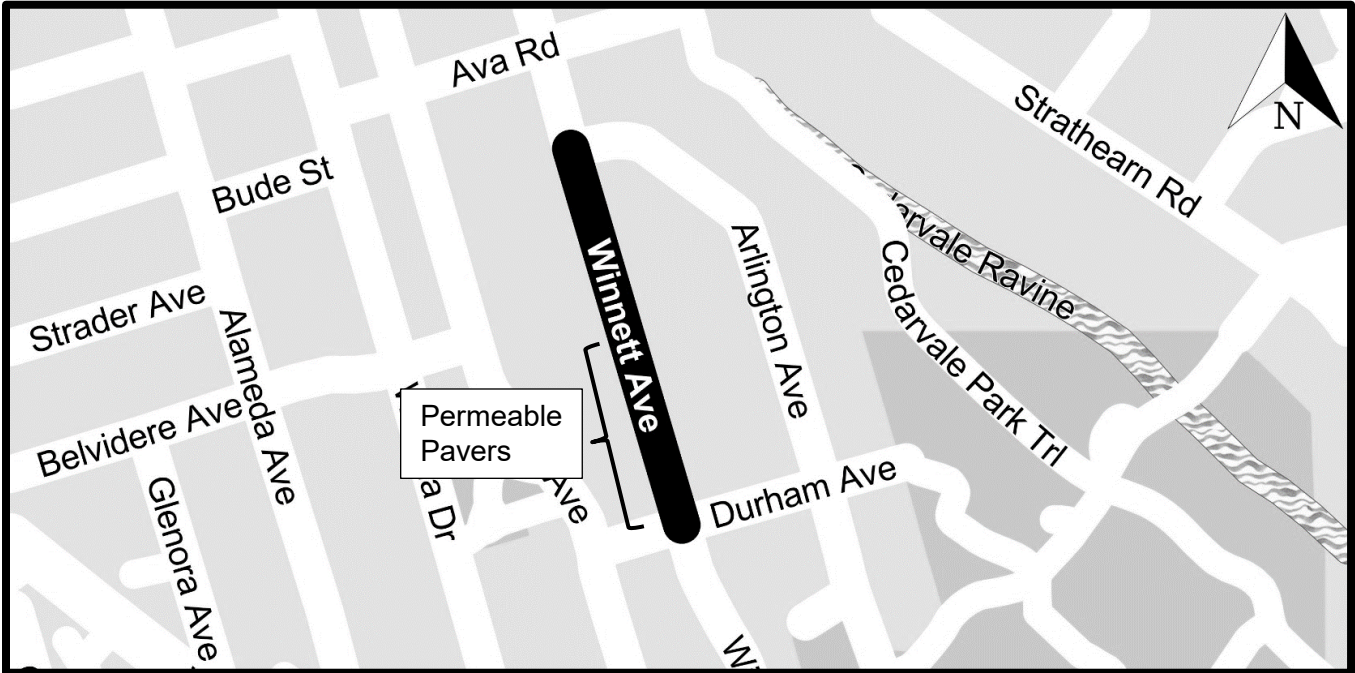

NEED MORE INFORMATION?

If you have questions about this construction project, please contact staff listed below, if you need to speak with staff on the construction site – please ask for the site inspector, respect physical distancing and wear a mask.

Contract	20ECS-TI-02LR
Project Manager	Anisha Patel, 416-392-7829, Anisha.Patel@toronto.ca
TTY Hearing Impaired Service	416-338-0889 (Daily 8 a.m. to 5 p.m., closed holidays)
General inquiries	311
Website	toronto.ca/torontospauls

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
