

November 24, 2022

Basement Flooding Protection Program Infrastructure Upgrades on Jane Street, Wilson Avenue and Other Local Roads

Contract: 19ECS-LU-01FP

Start Date: October 2020 Expected End Date: August 2023

**Timeline is subject to change.*

The City of Toronto is modifying and upgrading the storm and sanitary sewer system in your area in order to reduce surface and basement flooding. This work also involves replacing the city-owned portion of substandard water services and sanitary sewer laterals. Sidewalk repairs and accessibility improvements are also included on certain streets.

This project is part of the Council-approved 2020 Basement Flooding Protection Program to improve the water distribution system; renew our aging infrastructure and reduce the risk of sewer collapse or blockages that cause sewer backups and flooding.

WORK STATUS TO DATE

Work has resumed on Wilson Avenue. Work was delayed due to unforeseen construction variables that could not be anticipated until work had begun. Major underground work on Wilson Avenue should be completed by end of November 2022. Minor underground work on Wilson Avenue should be completed by end of December 2022 with restoration to follow.

Work is fully completed on Calvington Drive, Camborne Avenue, Dalsby Road, and Epsom Downs Drive.

Minor works remain on Canton Avenue, Exbury Road, Gatesgill Crescent, Letchworth Crescent, Tavistock Road, Troutbrooke Drive, and Tumpene Street. Note that these works will have minimal impacts to the public.

Restoration work that may include sod replacement, driveway reinstatement, curb installation, sidewalk section replacements, and paving operations are still to be completed on Buxton Road, Clevedon Street, Datchet Road, Dana Avenue, Deevale Road, Forthbridge Crescent, Julian Road, Lexfield Avenue, Monclova Road, Peacham Crescent, Smallwood Drive, and Westcliffe Road. Note that restoration cannot take place during winter months, and therefore it is likely that work on these streets will commence in early Spring 2023.

REMAINING WORK

Please find information below that outlines the remaining work for this contract. Remaining major sewer works are expected to be completed between November 2022 and August 2023.

Major Sewer Works	
Street	Remaining Work
Chalkfarm Drive	Storm sewers Storm service laterals Water services
Neames Crescent	Sanitary sewers Storm sewers Sewer service laterals Water services Inlet control devices
Jane Street	Sanitary sewers Storm sewers Sewer service laterals


Watermain and Service Works	
Street	Remaining Work
Heathrow Drive	Watermain Water services Road Resurfacing
Richard Clark Drive	Water services
Victory Drive	Watermain Water services
William Craig Drive	Water services Storm sewers
Wilson Avenue	Watermain Storm sewers Sewer service laterals

We anticipate that all remaining work listed above, including all restoration, will be completed by the end of Summer 2023. Thank you for your patience while we complete this important work.

WHAT TO EXPECT DURING CONSTRUCTION

- You may experience dust, noise and other inconveniences. The City will make efforts to reduce the impacts. We appreciate your patience.
- The City will not be responsible for damage to any privately owned items on City property.

MAP OF WORK AREA

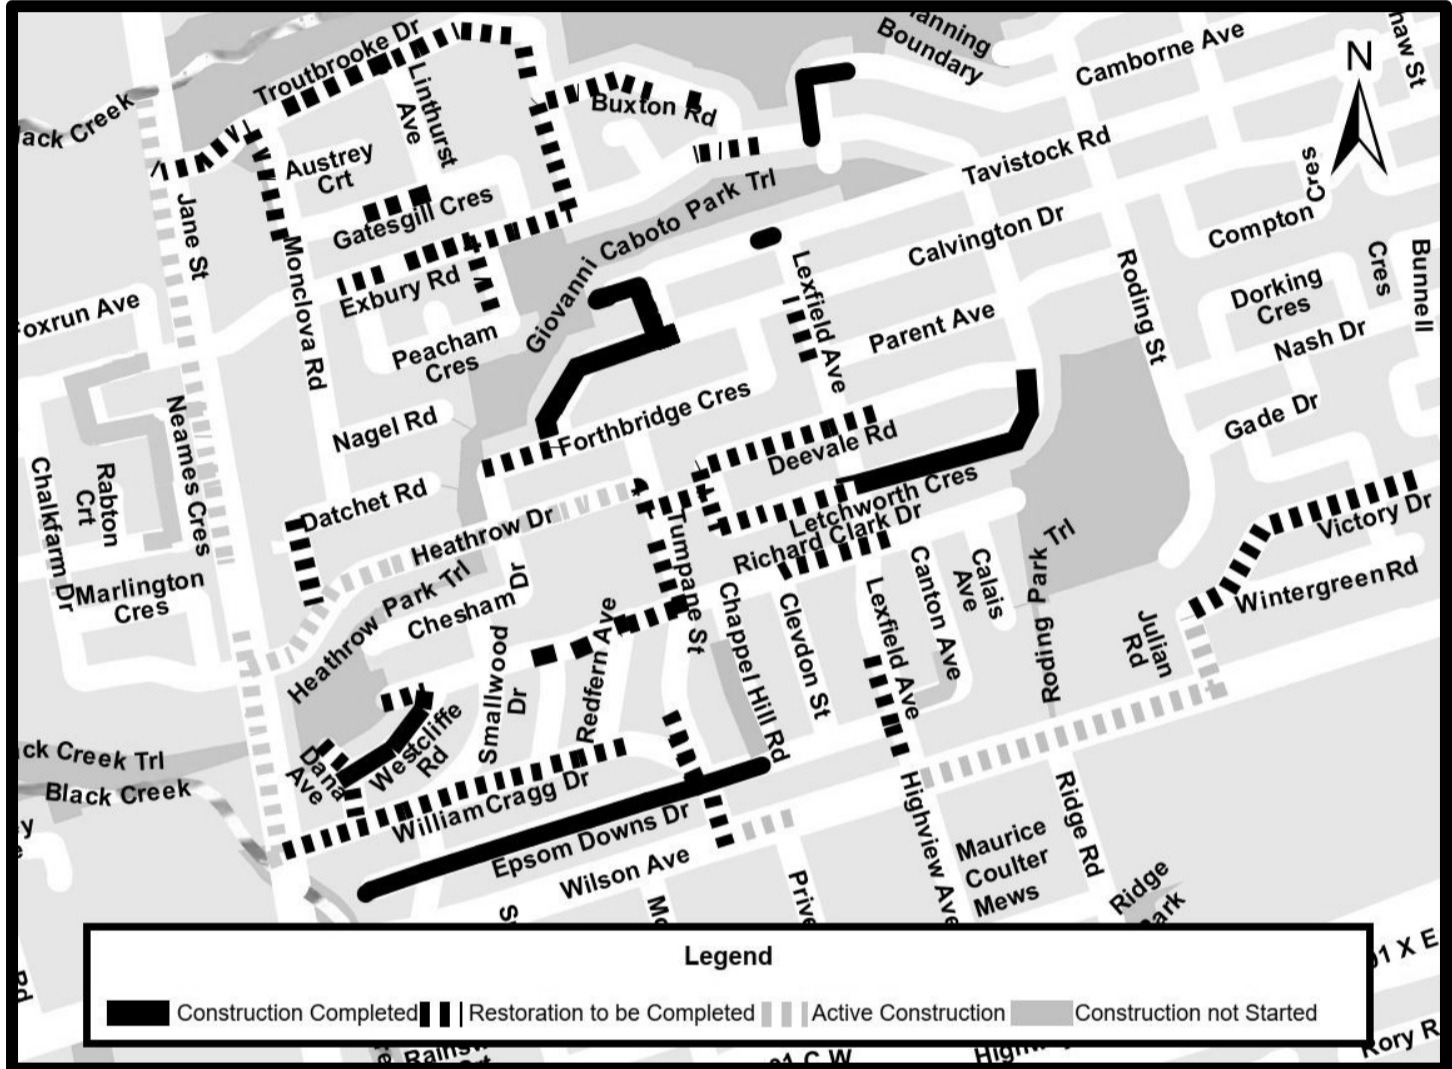

Contract	19ECS-LU-01FP
Field Ambassador	Shakha Vasdani and Max Morrison, 416-338-5497, bfp@toronto.ca
TTY Hearing Impaired Service	416-338-0889 (Daily 8 a.m. to 5 p.m., closed holidays)
General inquiries	311
Website	toronto.ca/improvements/ward6.htm or toronto.ca/improvements/ward7.htm

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait
