

February 14, 2023

Basement Flooding Protection Program Sanitary Sewer Upgrades and Watermain Replacement on Sheppard Avenue and other Local Roads

Contract: 19ECS-LU-12FP

Start Date: September 2021

Originally Forecast Completion: February 2023; NEW Completion Forecast: May 2023

Timeline is subject to change.

The City of Toronto is modifying and upgrading sanitary sewer and watermain system in your area to reduce surface and basement flooding. This work also involves replacing the City-owned portion of substandard water services and sanitary sewer laterals. Sidewalk repairs and accessibility improvements are also included on certain streets.

This project is part of the Council-approved 2021 Basement Flooding Protection Program to improve the water distribution system, renew our aging infrastructure and reduce the risk of sewer collapse or blockages that cause sewer backups and flooding.

WORK STATUS TO DATE

Work is active on Sheppard Avenue. However, due to unforeseen construction issues that became apparent after the work had begun, this has caused a delay. Major underground work on Sheppard Avenue should now be completed by the end of May 2023.

Underground work is fully completed on Beaver Valley Road, Brighton Avenue, Clifton Avenue, Combe Avenue, Goddard Street, Hove Street, Maxwell Street, Overbrook Place, Searle Avenue and Shaftesbury Avenue - with some restoration work remaining.

Restoration work may include sod replacement, driveway reinstatement, curb installation, sidewalk section replacements, and paving operations. Note that restoration cannot take place during winter months, and therefore it is likely that work on these streets will commence in early Spring 2023.

REMAINING WORK


Please find information below of the remaining work for this contract. The remaining major sewer work is expected to be completed by May 2023.

Street	Remaining Work
Sheppard Avenue	Sanitary sewers and laterals Restoration

WHAT TO EXPECT DURING CONSTRUCTION

- You may experience dust, noise, and other inconveniences. The City will make efforts to reduce those impacts. We appreciate your patience.
- The City will not be responsible for damage to any privately owned items on City property.

MAP OF WORK AREA

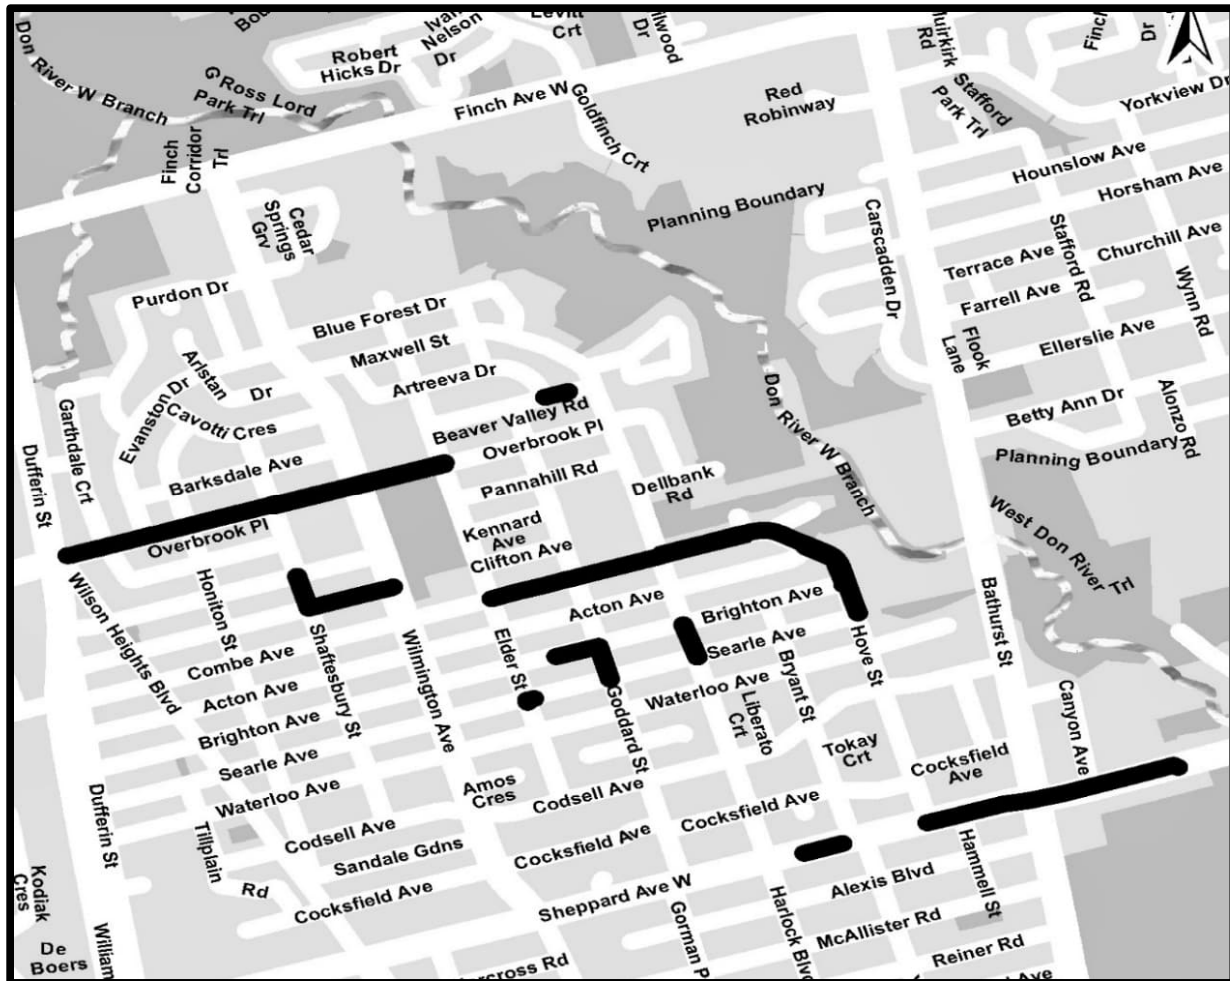

NEED MORE INFORMATION?

If you have questions about this construction project, please contact staff listed below. If you need to speak with staff on the construction site – please ask for the site inspector, respect physical distancing, and wear a mask.

Contract	19ECS-LU-12FP
Field Ambassador	Janet Webster, 416-338-5497, bfpp@toronto.ca
TTY Hearing Impaired Service	416-338-0889 (Daily, 8 a.m. to 5 p.m., closed holidays)
General inquiries	311
Website	toronto.ca/yorkcentre.ca

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
