

April 12, 2023


Watermain Replacement on Mildenhall Road from Rothmere Drive to Braeside Road

Contract: 22ECS-LU-07SU
 Start Date: August 12, 2022
 Restart Date: April 17, 2023
 End Date: June 5, 2023
**Timeline is subject to change.*

This notice provides an update on the replacement of the watermain and the City-owned portion of substandard water services on Mildenhall Road from Rothmere Drive to Braeside Road. Work on this project is currently behind schedule. Since the remaining work can only be completed during favourable weather conditions, the restoration activities are expected to resume on April 17, 2023, and has an end date of June 5, 2023.

We know this project has an impact to all businesses and residents along Mildenhall Road. We sympathize and appreciate your patience with the dust, noise, fencing and other inconveniences.

MAP OF WORK AREA

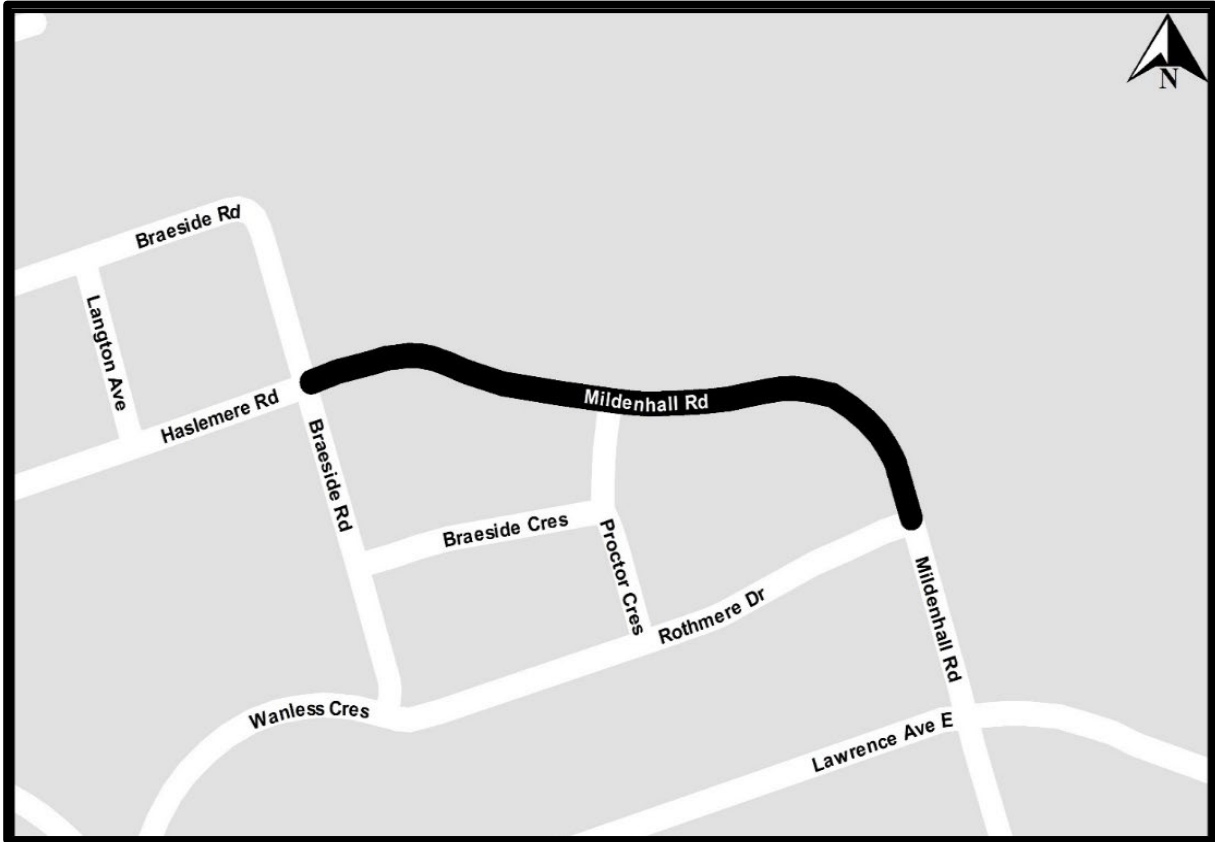

WORK STATUS TO DATE

- The City's contractor has:
- Completed the watermain installation.
 - Completed the water service connections.
 - Completed temporary restoration.

REMAINING WORK

- The City's contractor will complete:
- Permanent restoration of concrete sidewalks, curbs, and driveways.
 - Milling of asphalt, utility adjustments and base repairs.
 - Paving of asphalt.
 - Routing and sealing, and pavement marking.
 - Sod repairs.

NEED MORE INFORMATION?

If you have questions about this construction project, please contact staff listed below. If you need to speak with staff on the construction site – please ask for the site inspector, respect physical distancing and wear a mask.

Contract	22ECS-LU-07SU
Field Ambassador	Sunil Issac, 289-314-3127, field.ambassador2@GHD.com
TTY Hearing Impaired Service	416-338-0889 (Daily 8 a.m. to 5 p.m., closed holidays)
General inquiries	311
Website	toronto.ca/DonValleyWest

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
