


Woodbine Avenue Bridge Rehabilitation under Metrolinx Rail

Contract: 24ECS-BE-13PM
 Start Date: October 28, 2024 Expected End Date: April 2025
NEW End Date: August 2025*
**Timeline is subject to change.*

This notice provides an update on the rehabilitation of Woodbine Avenue under Metrolinx Rail, north of Gerrard Street East. Work on this project is currently behind schedule due to more structural deterioration than previously anticipated. The City's contractor continues to work diligently to complete the remainder of the project.

We acknowledge that this project has impacted businesses and residents along Woodbine Avenue. We sympathize and appreciate your patience and understanding with the dust, noise, fencing and other inconveniences.

MAP OF WORK AREA

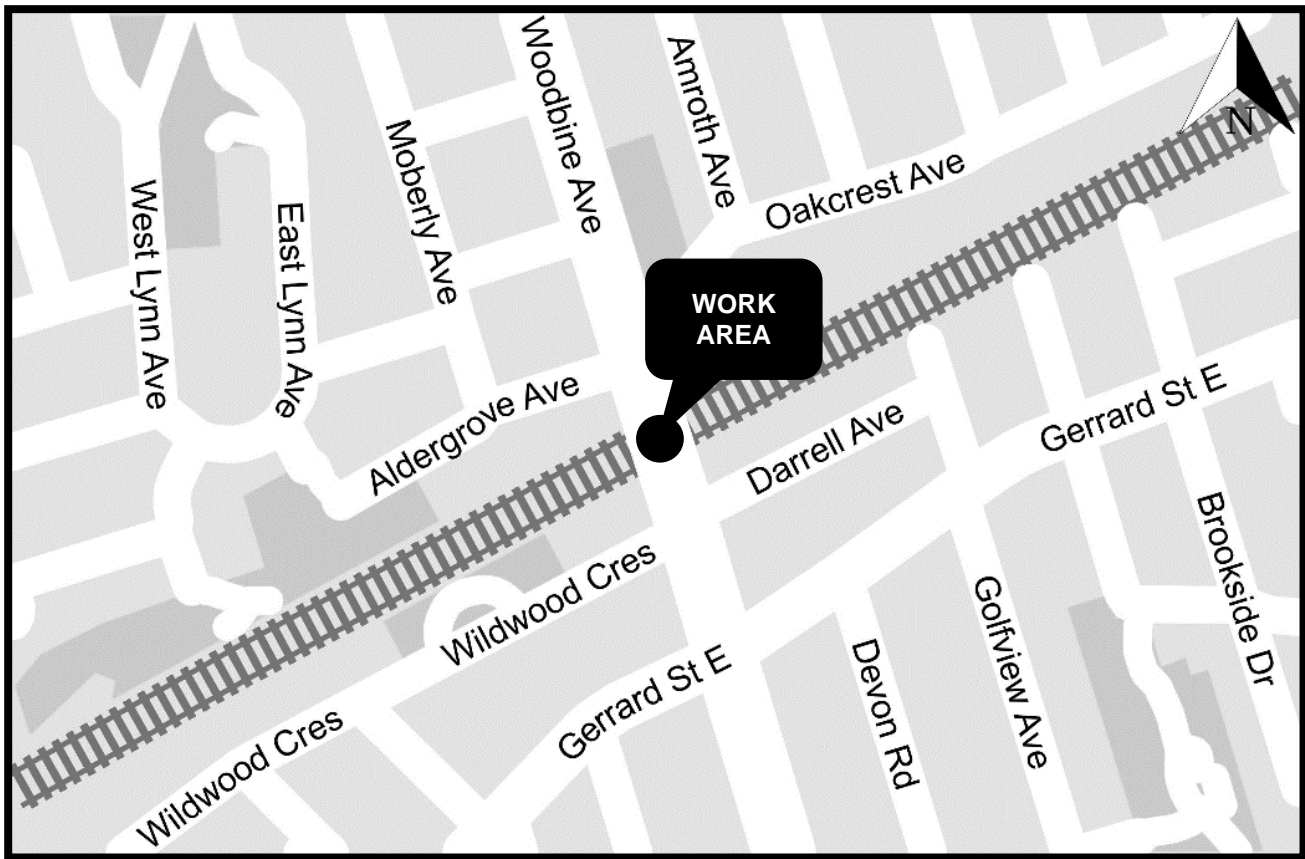

WORK STATUS TO DATE

- To date, the following work has been completed:
- Refaced concrete abutment walls, wingwalls, and sidewalk supporting walls on the east side
 - Reconstructed east elevated concrete sidewalks and installed new pedestrian railings
 - Completed patch repairs and crack injection on the east span deck soffit and pier
 - Replace luminaires and conduits under the bridge on the east span

REMAINING WORK

- In the coming months, the City's contractor will be completing the following work:
- Reface the west side concrete abutment walls, wingwalls, and sidewalk supporting walls
 - Reconstruct west elevated concrete sidewalks with new pedestrian railings
 - Patch repair and crack injection of the west span deck soffit and pier
 - Reconstruct the crash protection at the south end of the bridge pier
 - Replace west span luminaires and conduits under the bridge
 - Restore roadway pavement markings

NEED MORE INFORMATION?

If you have questions about this construction project, please contact staff listed below.

Contract	24ECS-BE-13PM
Field Ambassador	Maria Lippa, 416-495-4213, WoodbineAveUnderMx@morrisonhershfield.com
Deaf, Hard of hearing and Hearing impaired service	Telecommunications Relay Service (TRS) Dial 711 (24/7)
General inquiries	311
Website	toronto.ca/beacheseastyork

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
