


Telecom Events (past to present)

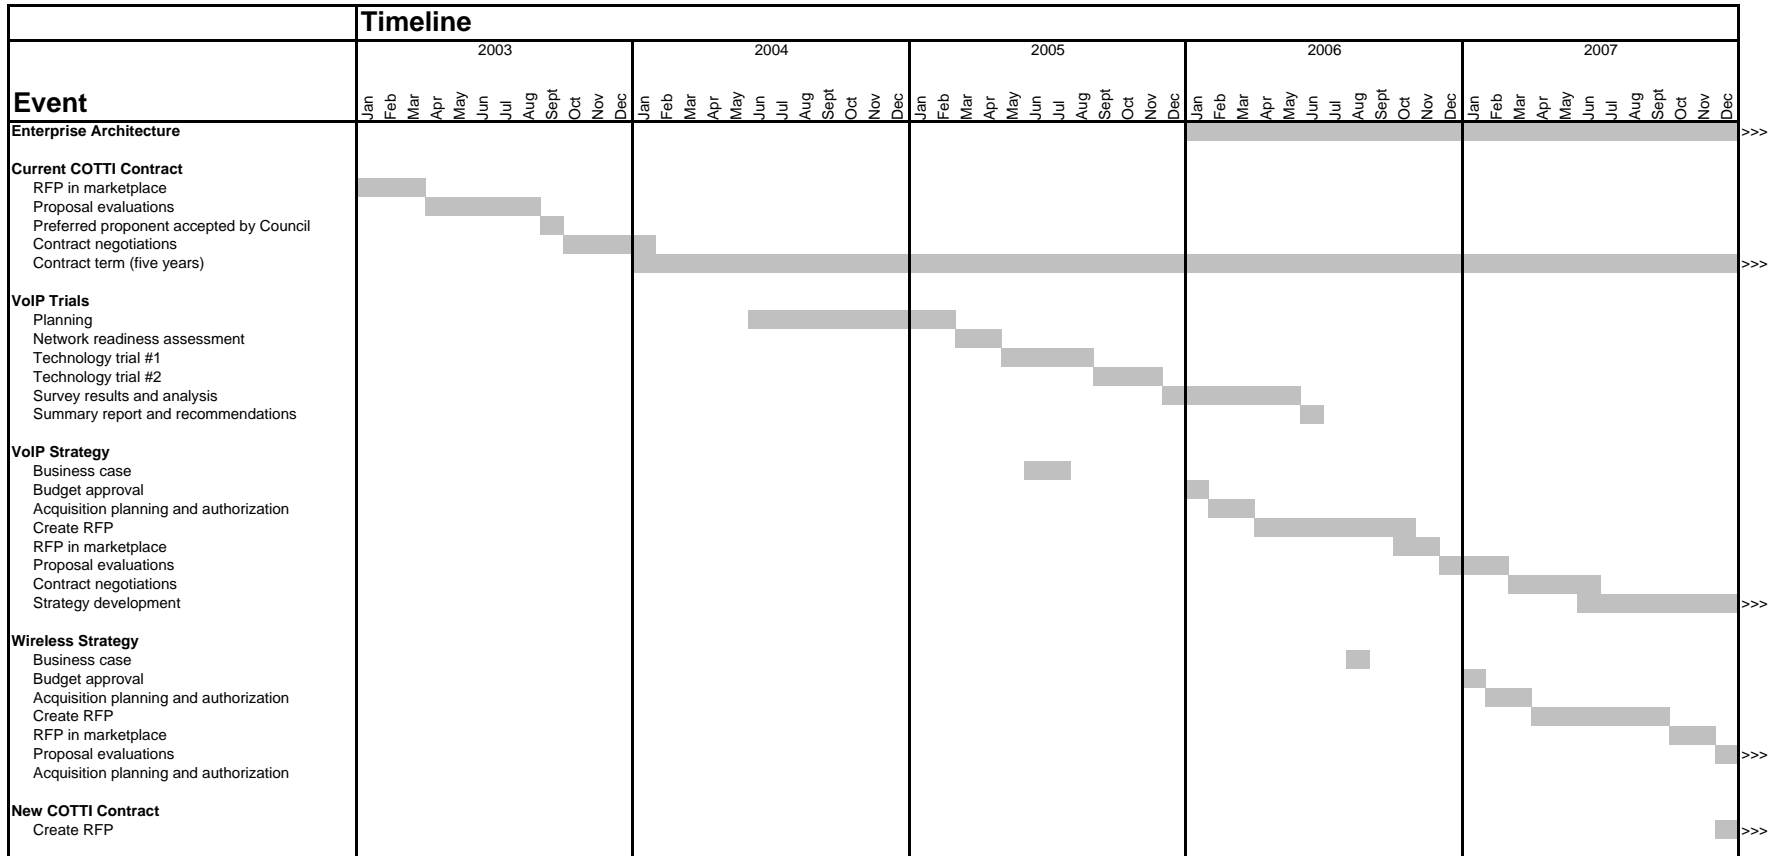

Telecom Events (next steps)

Event	Timeline																																															
	2008			2009			2010			2011			2012																																			
	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Enterprise Architecture																									>>																							
Current COTTI Contract																																																
Contract term (five years)																																																
Optional one year extension																																																
Optional one year extension																																																
VoIP Strategy																																																
Strategy development																																																
Report to BAP																																																
Report to GMC																																																
Report to Council																																																
Wireless Strategy																																																
Proposal evaluations																																																
Contract negotiations																																																
Strategy development																																																
Report to BAP																																																
Report to GMC																																																
Report to Council																																																
New COTTI Contract																																																
Create RFP																																																
Integrate VoIP Strategy																																																
Integrate Wireless Strategy																																																
RFP in marketplace																																																
Proposal evaluations																																																
Report to BAP																																																
Report to GMC																																																
Report to Council																																																
Contract negotiations																																																
Contract term																									>>>																							
VoIP Implementation																																																
Planning																																																
Business case																																																
Budget approval																																																
Acquisition planning and authorization																																																
Design																																																
Procure																																																
Implement pilot																																																
Rollout (under new contract with incumbent)																									>>>																							
Rollout (under new contract not incumbent)																																																
